
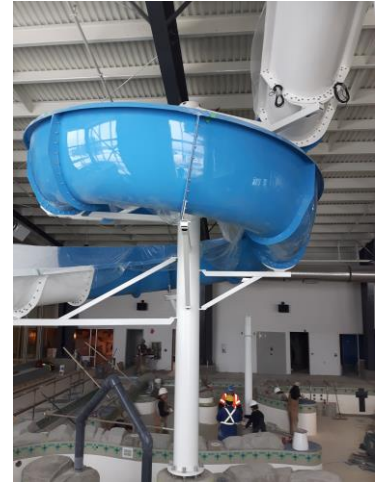


JMCC AQUATIC FACILITY BI-WEEKLY UPDATE

February 6, 2018

Progress This Week (Week ending February 9, 2018)

- Feature rocks were completed around the slide base and leisure pool.
- Washroom partitions are ongoing.
- Concrete pours for the tiered benches were completed.
- Sound baffles were completed in the Natatorium.
- Millwork was installed in the party room and washroom/changeroom areas.
- Tile install on the Natatorium pool deck is underway.

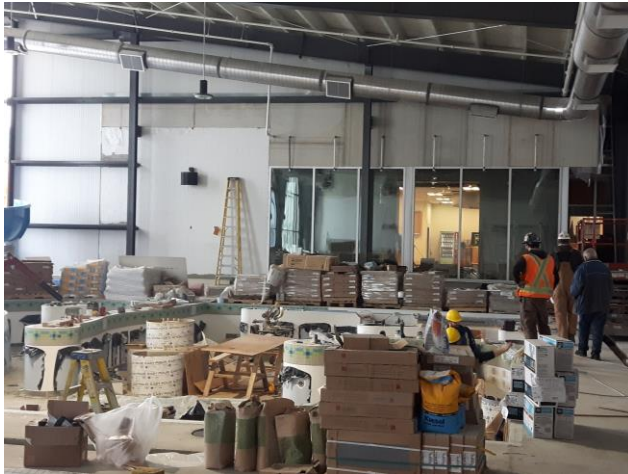

Upcoming Work Next Week (Week ending February 16, 2018)

- Locker install will be underway.
- New entrance door will be installed on Tuesday February 13th.
- Pool membranes will be underway.
- Trench drains will be installed ahead of the tile installers.
- Interior curtain wall glazing will be completed.

